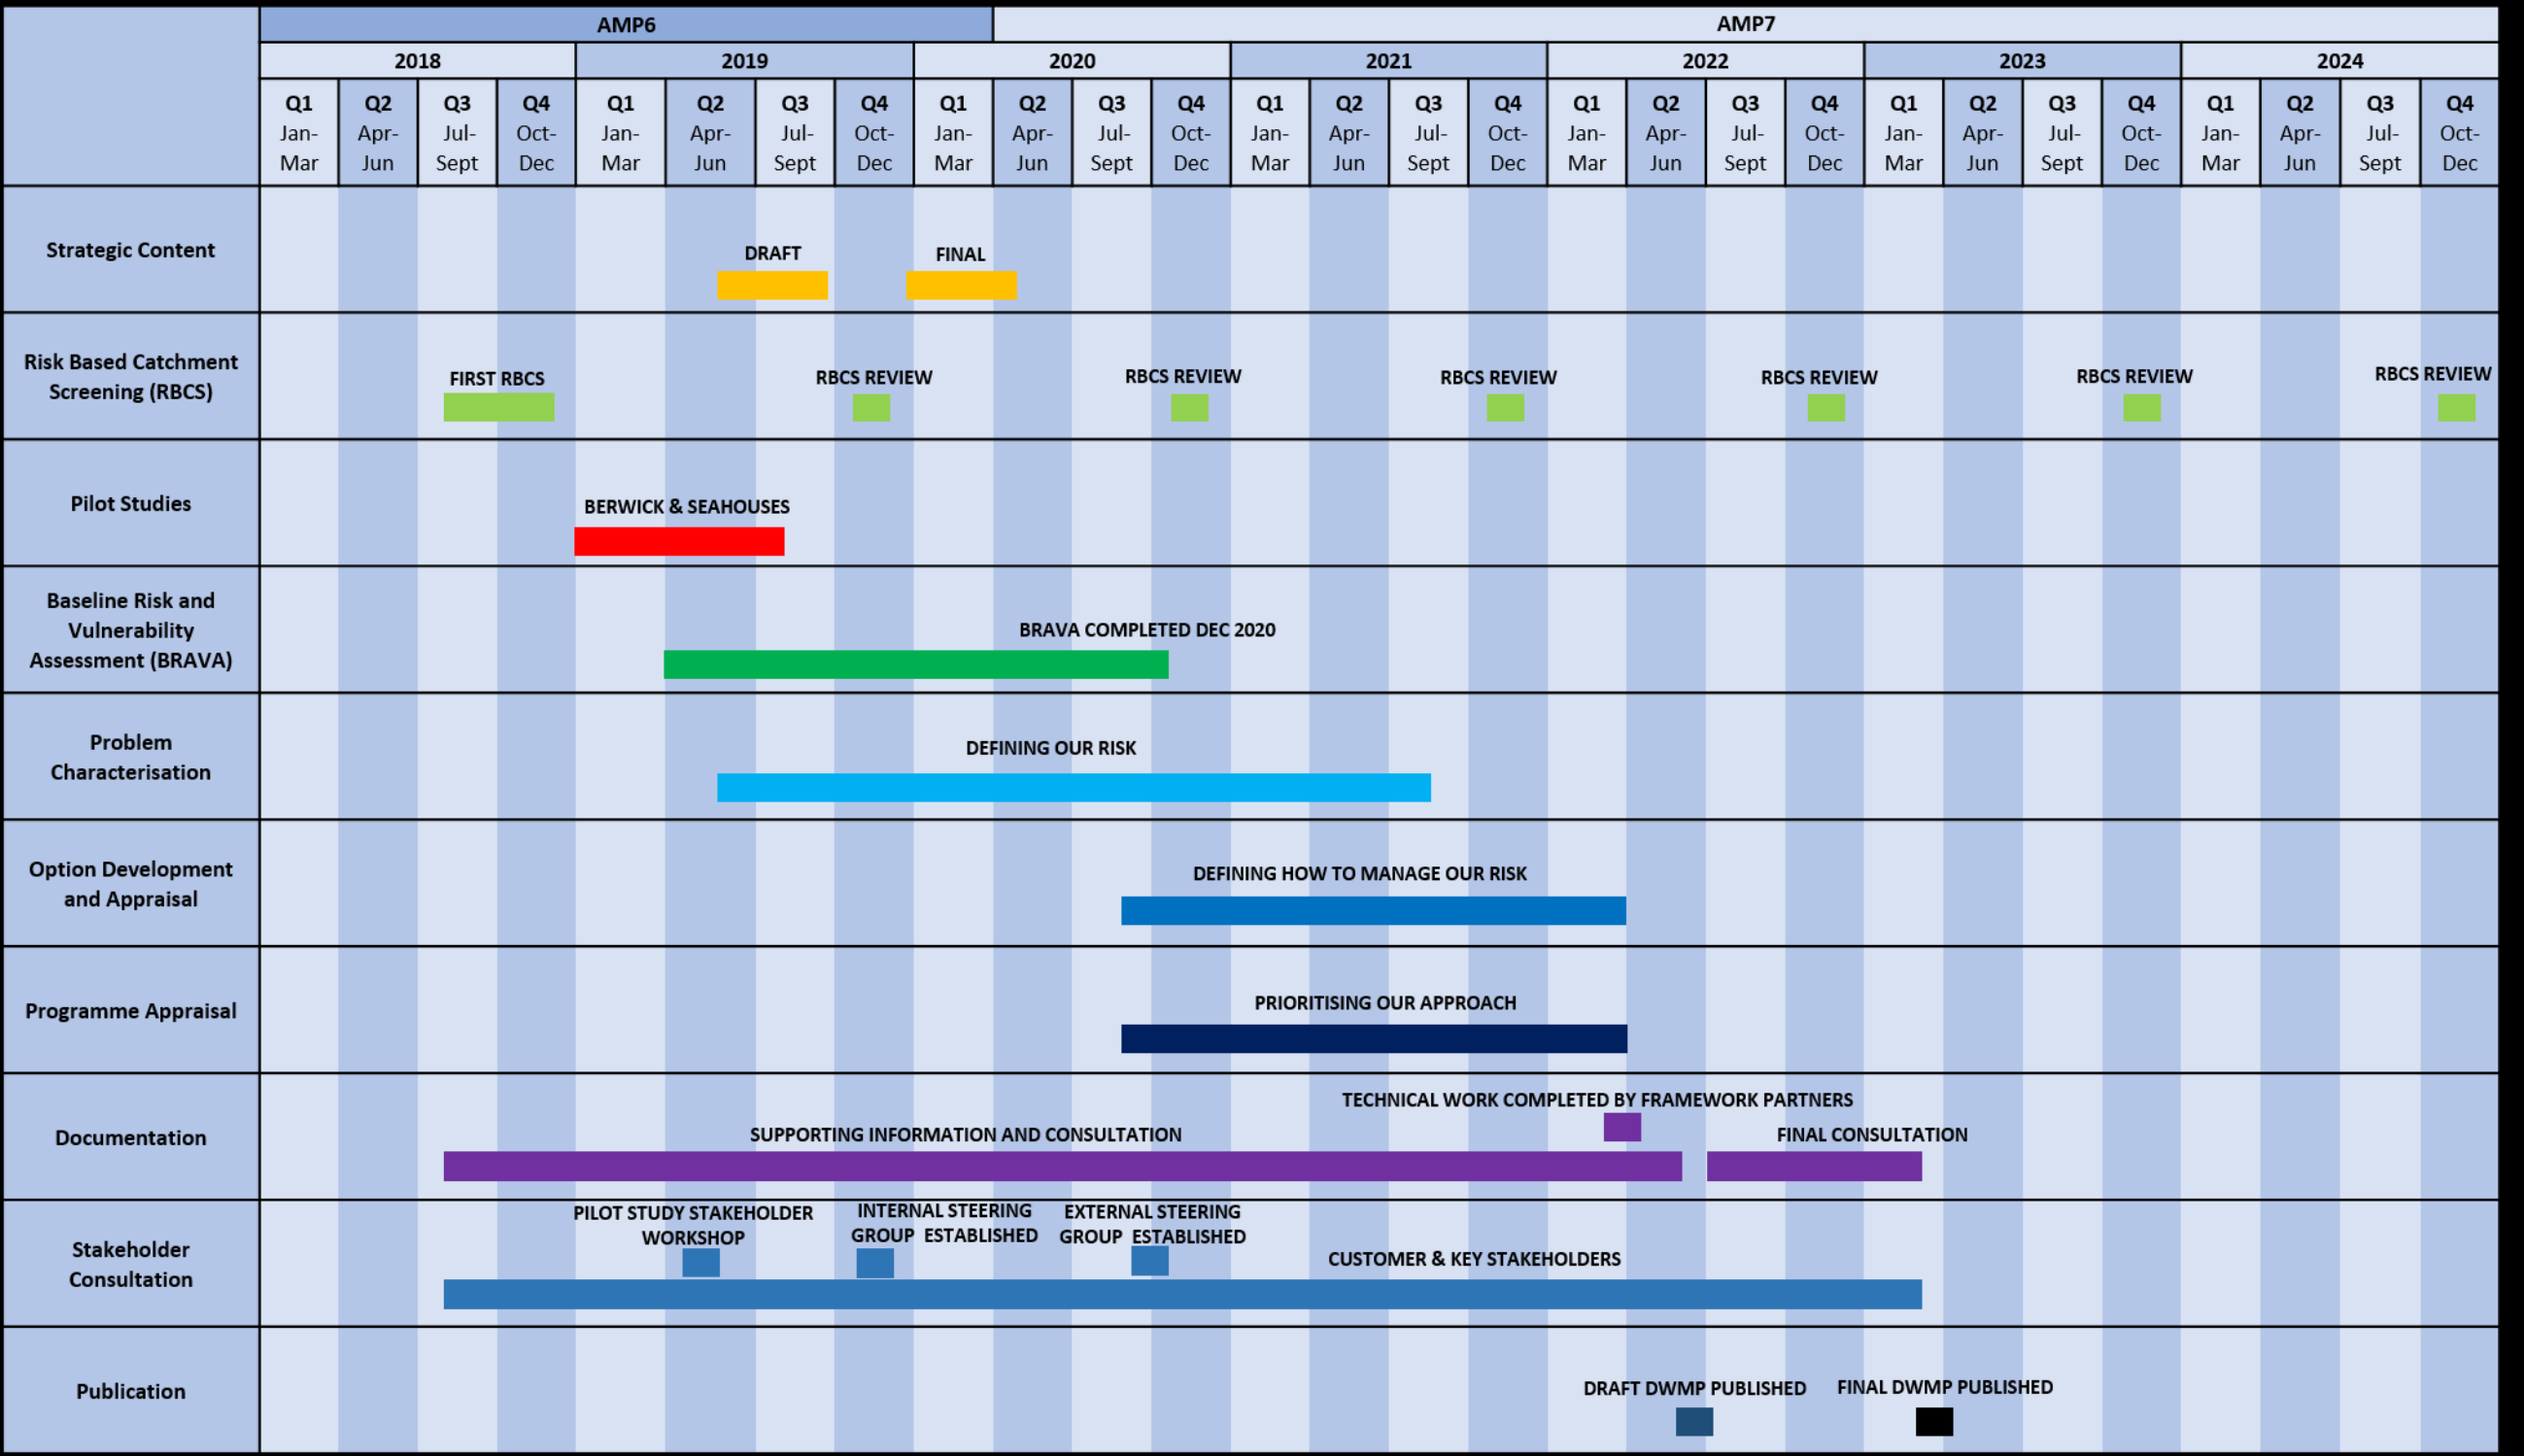
AMP6
AMP7
2018
2019
2020
2021
2022
2023
2024
Q1 Jan-Mar
Q2 Apr-Jun
Q3 Jul-Sept
Q4 Oct-Dec
Strategic Content
DRAFT
FINAL
Risk Based Catchment Screening (RBCS)
FIRST RBCS
RBCS REVIEW
RBCS REVIEW
RBCS REVIEW
RBCS REVIEW
RBCS REVIEW
RBCS REVIEW
Pilot Studies
BERWICK & SEAHOUSES
Baseline Risk and Vulnerability Assessment (BRAVA)
BRAVA COMPLETED DEC 2020
Problem Characterisation
DEFINING OUR RISK
Option Development and Appraisal
DEFINING HOW TO MANAGE OUR RISK
Programme Appraisal
PRIORITISING OUR APPROACH
Documentation
TECHNICAL WORK COMPLETED BY FRAMEWORK PARTNERS
SUPPORTING INFORMATION AND CONSULTATION
FINAL CONSULTATION
Stakeholder Consultation
PILOT STUDY STAKEHOLDER WORKSHOP
INTERNAL STEERING GROUP ESTABLISHED
EXTERNAL STEERING GROUP ESTABLISHED
CUSTOMER & KEY STAKEHOLDERS
Publication
DRAFT DWMP PUBLISHED
FINAL DWMP PUBLISHED
